

New Fountain Hill Elementary School

Phase 1 – Abatement/Demolition

Phase 2 – Site

Phase 3 – Building

Notice to Proceed: March 24, 2025

Phase 1 Completion: September 10, 2025

Phase 2 Completion: January 2, 2026

Phase 3 Completion: August 20, 2027



PROJECT STATUS UPDATE

The project is currently meeting the Contract milestone dates.

Phase 1 - Abatement & Demolition:

- Playground was relocated to Donegan Elementary School.
- The generator, basketball backboards, and various other items have been salvaged as requested.
- Demolition of the existing Fountain Hill Elementary School continued through August. Spotts, Stevens, and McCoy continued to be onsite periodically taking air samples during demolition. The work is progressing as planned. Demolition of what remains of the building is expected to be completed during the first week of September. The demolition of the concrete foundation walls and footings will continue following the completion of the building demolition.




Playground Relocation and Mulch Installation Complete at Donegan Elementary School



Traffic and Pedestrian Signage Installed on Garden Street




Salvaged Center Court Logo from Gym Floor

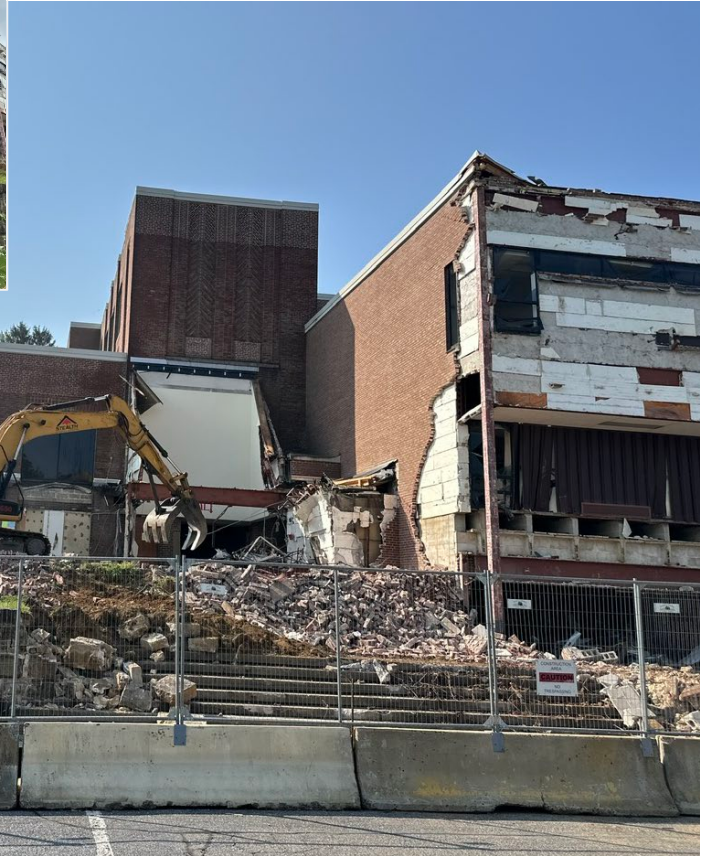

Demolition of the Administrative Office Area



Demolished Administrative Office Area

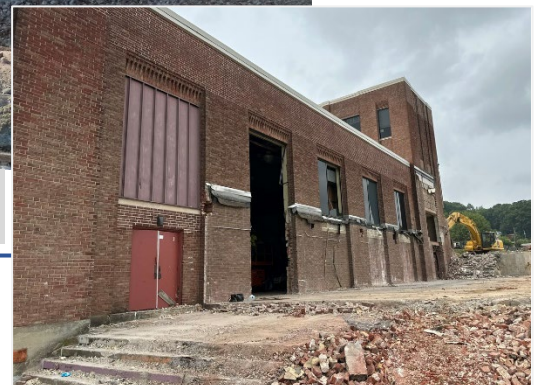



Continued Demolition of the Gymnasium



Drone View of Demolition of the Northwest Corner of the Building



Drone View of Building Demolition August 11, 2025



Drone View of Building Demolition August 28, 2025
